Activity ID	Activity Name	Orig Dur	Act % Comp	Start	Finish	BL Finish	Remaining Total Cost	evms rule	Total Float	ECP
NSTX Upgrade Project		9		08-May-14	21-May-14		$47,414.40		-48	
Job: 1305 - OHMIC Heating Coil (OH)-CHRZA		9		08-May-14	21-May-14		$47,414.40		-48	
TF/OH Fabrication		9		08-May-14	21-May-14		$47,414.40		-48	
CS High Bay		9		08-May-14	21-May-14		$47,414.40		-48	
1305-8800B	Lower/apply wet layup around U/L crown regions (cont 2 shft)	0	0%	08-May-14	08-May-14		$9,698.40	E	-48	04
1305-8800G	Install U/L TF fittings and bulkhead	0	0%	08-May-14	08-May-14		$16,164.00	E	-42	04
1305-8800H	Hydrostat TF fittings	0	0%	08-May-14	08-May-14		$4,310.40	E	-39	04
1305-8800E	Install upper silicone band between OH/TF (cont 2 shft)	0	0%	20-May-14	20-May-14		$4,310.40	E	-48	04
1305-8800F	Install belleville washer assly & reinst lwr sup (cont 2 shft)	0	0%	21-May-14	21-May-14		$12,931.20	E	-48	04

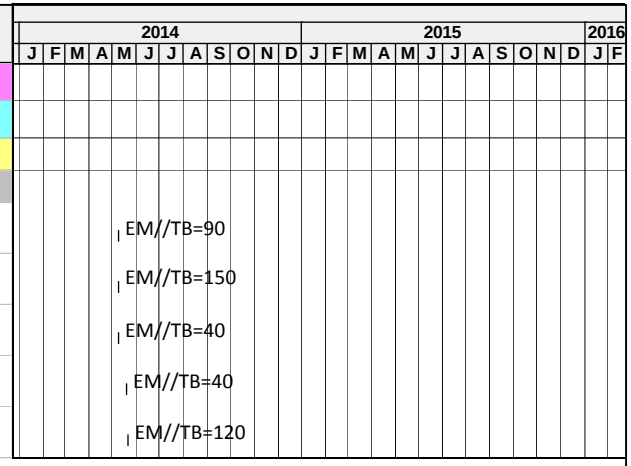

Actual Work
Critical Remaining Work
Remaining Work

NSTX-U ECP-105

 Run Date:12-Dec-13
